PROJECT MANAGEMENT

Prof. Dr. Zeynep IŞIK
Room: 1 – 55

Project Integration Management

- The Project Integration Management includes the processes and activities needed to identify, define, combine, unify and coordinate the various processes and project management activities within the Project Management Process Groups.

- In the project management context, integration includes characteristics of unification, consolidation, articulation, and integrative actions that are crucial to project completion, successfully managing stakeholder expectations, and meeting requirements.

Project Integration Management

- Project Integration Management entails making choices about resource allocation, making trade-offs among competing objectives and alternatives, and managing the interdependencies among the project management knowledge areas.

- The project management processes are usually presented as discrete processes with defined interfaces while, in practice, they overlap and interact.

Project Integration Management

- **Develop project charter:** Developing a document that formally authorizes a project or a phase and documenting initial requirements that satisfy the stakeholder's needs and expectations.

- **Develop project management plan:** Documenting the actions necessary to define, prepare, integrate and coordinate all subsidiary plans.

- **Direct and manage project execution:** Perform the work defined in project management plan

Project Integration Management

- **Monitor and control project work:** track, review and regulate the progress to meet the performance objectives.

- **Perform integrated change control:** Review all change requests and manage changes to the organizational process assets, project documents and project management plan.

- **Close project or phase:** Finalize all activities across all project management process groups.

Project Scope Management

- Project Scope Management includes the processes required to ensure that the project includes all the work required and only the work required, to complete the project successfully.

- Managing the project scope is primarily concerned with defining and controlling what is and what is not included in the project.

- In the project context, the term scope can refer to:
  - Product scope: the features and functions that characterize a product, service or result.
  - Project scope: the work needs to be accomplish to deliver a product service or result.


Project Scope Management

- **Collect requirements:** Define and document stakeholders' needs to meet the project objectives.

- **Define scope:** Develop a detailed description of the project and product

- **Create Work Breakdown Structure (WBS):** Subdivide project deliverables and project work into smaller, more manageable components.

Work Breakdown Structure

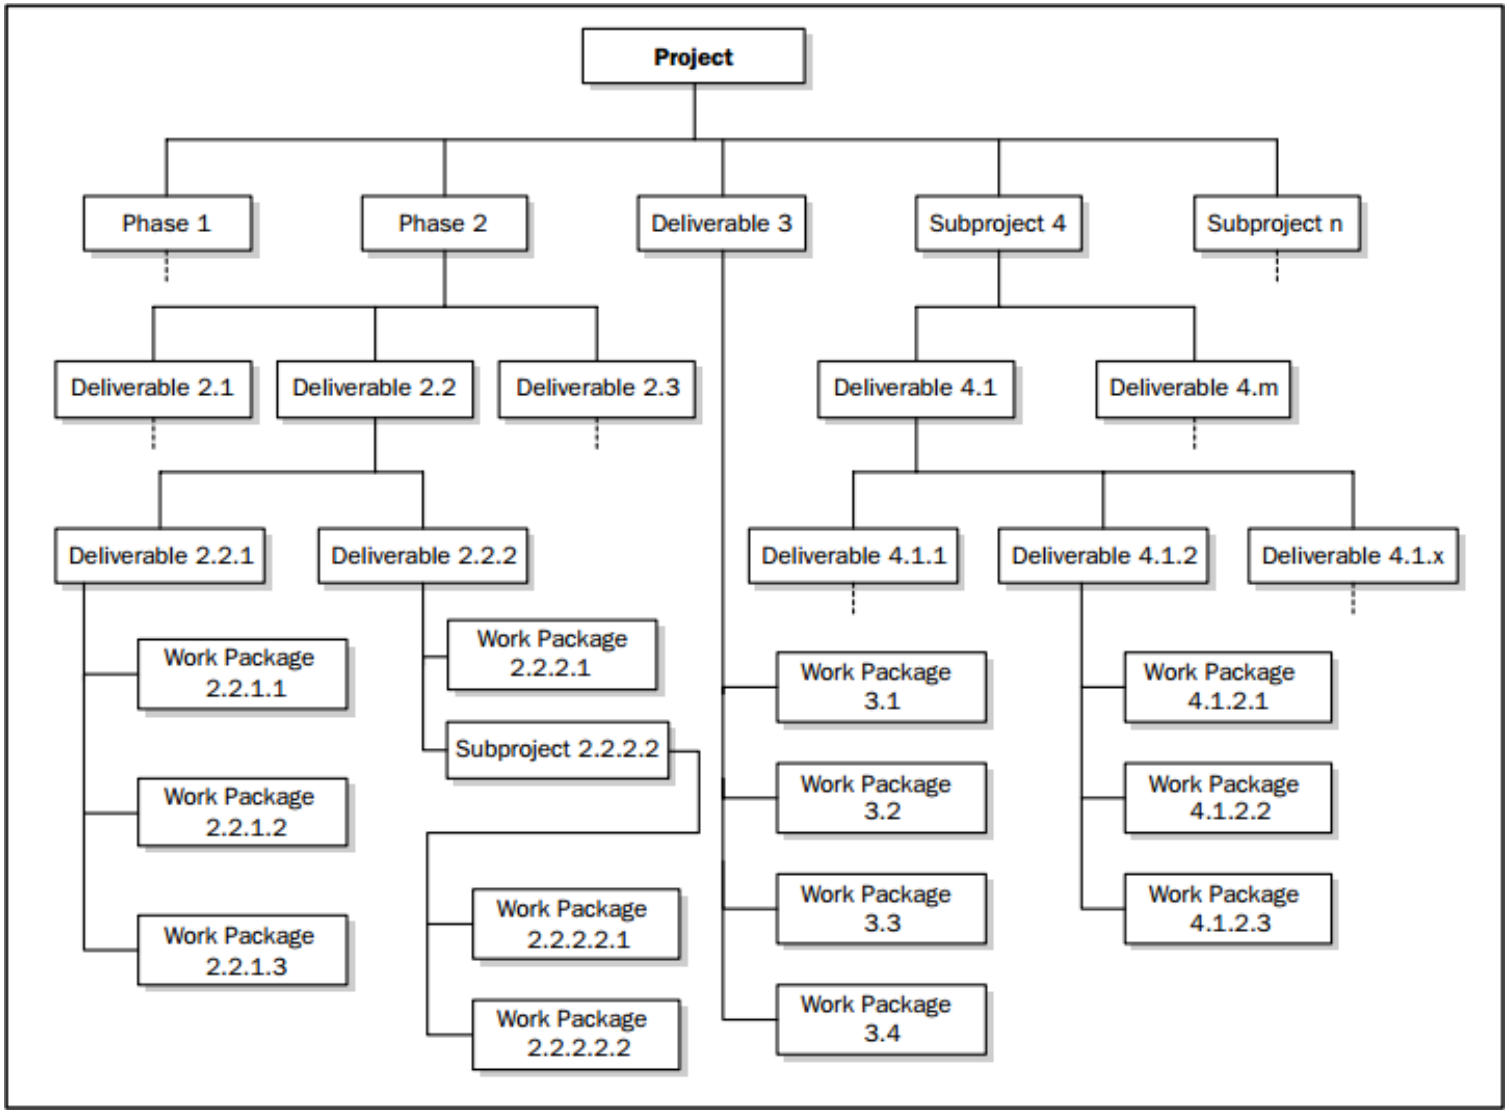

Project Scope Management

- **Verify scope:** Formalize acceptance of the completed project deliverables.

- **Control scope:** Monitor the status of the project and product scope and manage changes to the scope baseline.

Project Time Management

- The Project Time Management processes include the following:
  - Activity definition- process of identifying the specific actions to be performed to produce the project deliverables
  - Activity sequencing-process of identifying and documenting the relationships among the project activities
  - Activity resource estimating – process of estimating the type and quantities of material, people, equipment or supplies required to perform each activity.

Project Time Management

- Activity duration estimation- process of approximating the number of work periods needed to complete the individual activities with the estimated resources.


- Schedule development – process of analyzing activity sequences, durations, resource requirements, and schedule constraints to create the project schedule.

- Schedule control - process of monitoring the status of the project to update project progress and manage changes to schedule baseline.

Project Cost Management

- Project Cost Management includes the processes involved in planning, estimating, budgeting and controlling costs so that the project can be completed within the approved budget.
  - Cost estimating – developingan approximationof the monetary resources needed to complete project activities.
  - Cost budgeting – aggregatingthe estimated costs of individual activities or work packages to establish an authorized cost baseline.
  - Cost control – monitoring the status to the project to update budget and managing changes to the cost baseline.

Project Cost Management

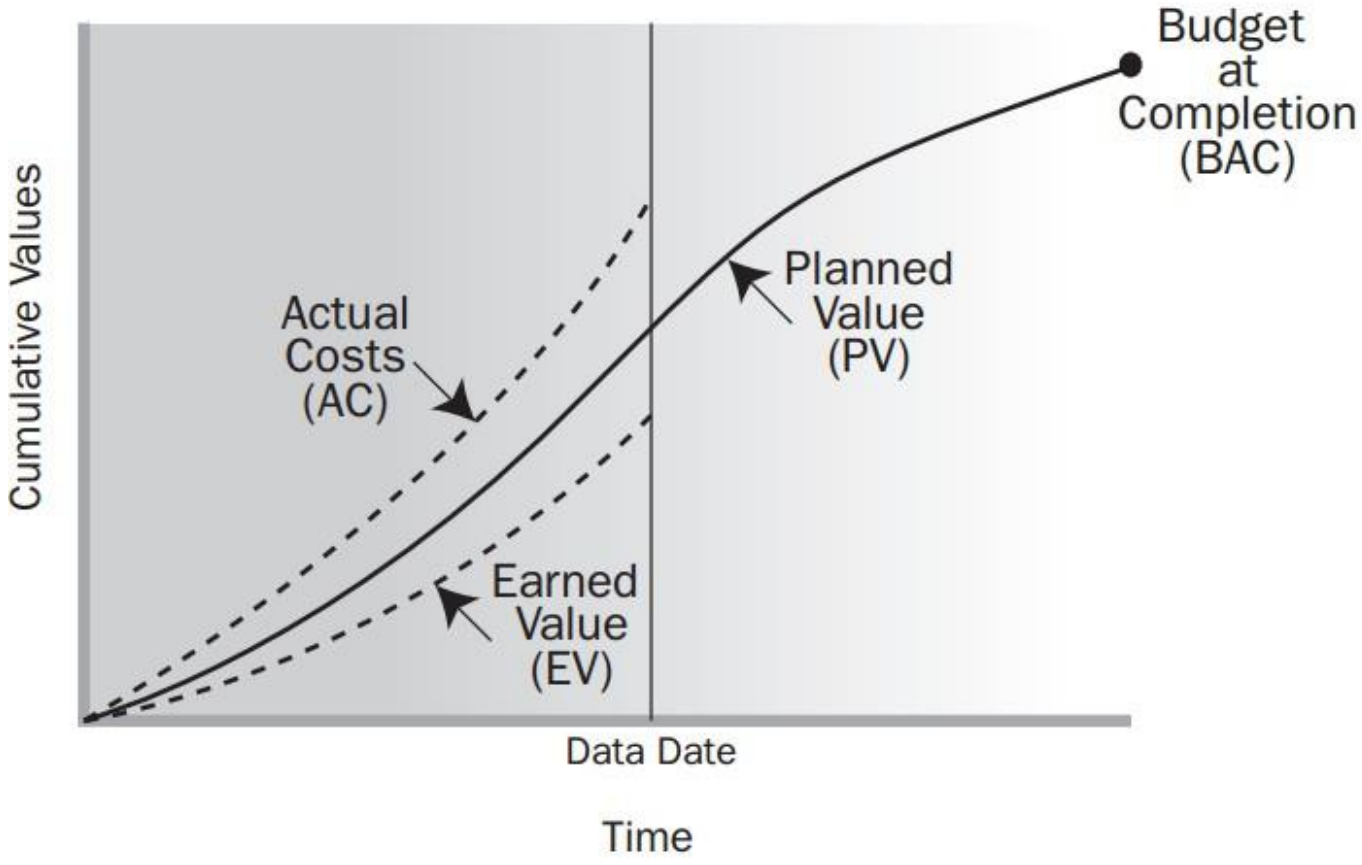

Project Quality Management

- Project Quality Management processes include all the activities of the performing organization that determine quality policies, objectives and responsibilities so that the project will satisfy the needs for which it was undertaken.
  - Plan Quality – process of identifying quality requirements and/or standards for the project and product, and documenting how the project will demonstrate compliance.
  - Perform Quality Assurance – process of auditing the quality requirements and the results from quality control measurements to ensure appropriate quality standards and operational definitions are used.
  - Perform Quality Control – process of monitoring and recording the results of executing the quality activities to assess performance and recommend necessary changes.

Project Resource Management

- Project Resource Management includes the processes to identify, acquire, and manage the resources needed for the successful completion of the project.

- These processes help ensure that the right resources will be available to the project manager and project team at the right time and place.

Project Resource Management

- The Project Resource Management processes are:
  - Plan Resource Management—The process of defining how to estimate, acquire, manage, and utilize physical and team resources.
  - Estimate Activity Resources—The process of estimating team resources and the type and quantities of material, equipment, and supplies necessary to perform project work.
  - Acquire Resources—The process of obtaining team members, facilities, equipment, materials, supplies, and other resources necessary to complete project work.

Project Resource Management

- Develop Team—The process of improving competencies, team member interaction, and the overall team environment to enhance project performance.
- Manage Team—The process of tracking team member performance, providing feedback, resolving issues, and managing team changes to optimize project performance.
- Control Resources—The process of ensuring that the physical resources assigned and allocated to the project are available as planned, as well as monitoring the planned versus actual use of resources, and performing corrective action as necessary.

Project Communications Management

- Project Communications Management is the Knowledge area that employs the processes required to ensure timely and appropriate generation, collection, distribution, storage, retrieval and ultimate disposition of project information.
  - Identify Stakeholders - involves the identification of all stakeholders that can impact the project. This Project Management Communication process involves documenting their level of interest, power, influence, and project impact.
  - Plan Communications - involves documenting the communication needs of the stakeholders identified in the Identify Stakeholders process.

Project Communications Management

- Distribute Information – involves making relevant information available to project stakeholders as planned.

- Manage Stakeholder Expectations - involves using the various communication methods, interpersonal skills and management skills to ensure the communication needs of stakeholders are met.

- Report Performance - involves ensuring performance, progress and forecast information are communicated to the identified stakeholders.

Project Risk Management

- Project Risk Management includes the processes concerned with conducting risk management planning, identification, analysis, responses and monitoring and control on a project.
- Objective: increase the probability and impact of positive events, and decrease the probability and impact of negative events.
  - Plan risk management – process of defining how to execute the risk management activities of a project
  - Identify risks – process of determining which risks may affect the project and documenting their characteristics.

- Perform qualitative risk analysis – process of prioritizing risks for further analysis or action by assessing and combining their probability of occurrence and impact.
- Perform quantitative risk analysis – process of numerically analyzing the effect of identified risks on overall project objectives.
- Plan risk responses – process of developing options and actions to enhance opportunities and to reduce threats to project objectives.
- Monitor and control risks – process of implementing risk response plans, tracking identified risks, monitoring residual risks, identifying new risks, and evaluating risk process effectiveness throughout the project.

Project Procurement Management

- Project Procurement Management includes the processes to purchase or acquire the products, services or results needed from outside the project team to perform the work.

  - Plan procurements - documenting purchasing decisions, specifying the approach and identifying the potential sellers
  - Conduct procurements - obtaining seller responses, selecting a seller and awarding a contract
  - Administer procurements - – managing procurement relationships, monitoring contract performance, and making changes and corrections as needed
  - Close procurements - completing each project procurement

Project Stakeholder Management

- Project Stakeholder Management includes the processes required to identify the people, groups, or organizations that could impact or be impacted by the project, to analyze stakeholder expectations and their impact on the project, and to develop appropriate management strategies for effectively engaging stakeholders in project decisions and execution.


Project Stakeholder Management


- Identify Stakeholders—The process of identifying project stakeholders regularly and analyzing and documenting relevant information regarding their interests, involvement, interdependencies, influence, and potential impact on project success.
- Plan Stakeholder Engagement—The process of developing approaches to involve project stakeholders based on their needs, expectation, interests, and potential impact on the project.
- Manage Stakeholder Engagement—The process of communicating and working with stakeholders to meet their needs and expectations, address issues, and foster appropriate stakeholder engagement involvement.
- Monitor Stakeholder Engagement—The process of monitoring project stakeholder relationships and tailoring strategies for engaging stakeholders through the modification of engagement strategies and plans.

Project Management Life Cycle


- Project Life Cycle
- Project Management Life Cycle

Project Management Life Cycle Methods

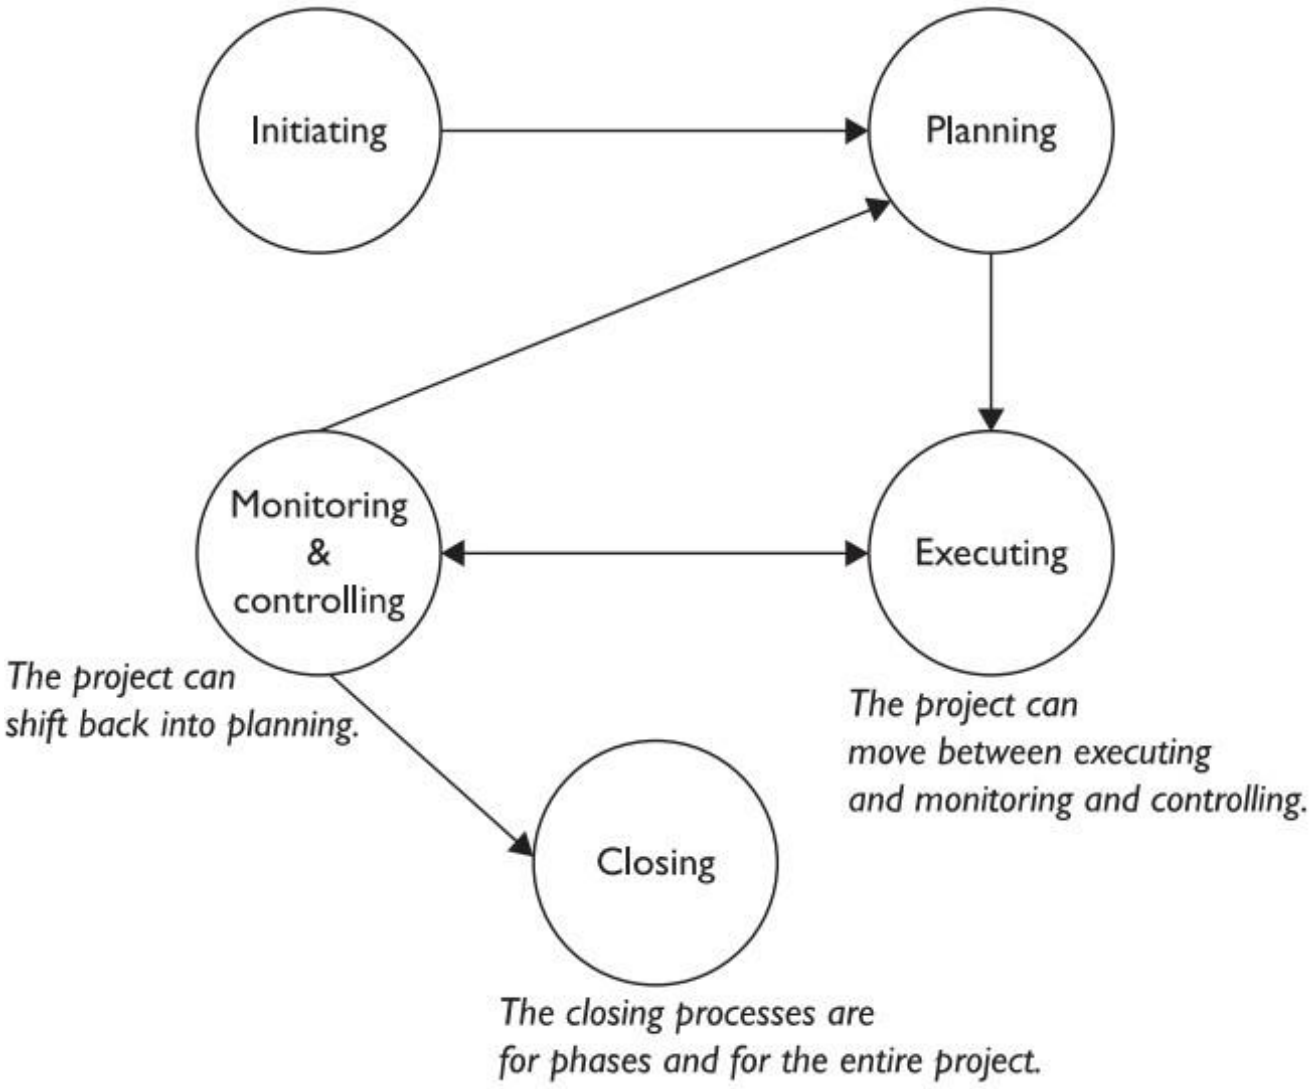

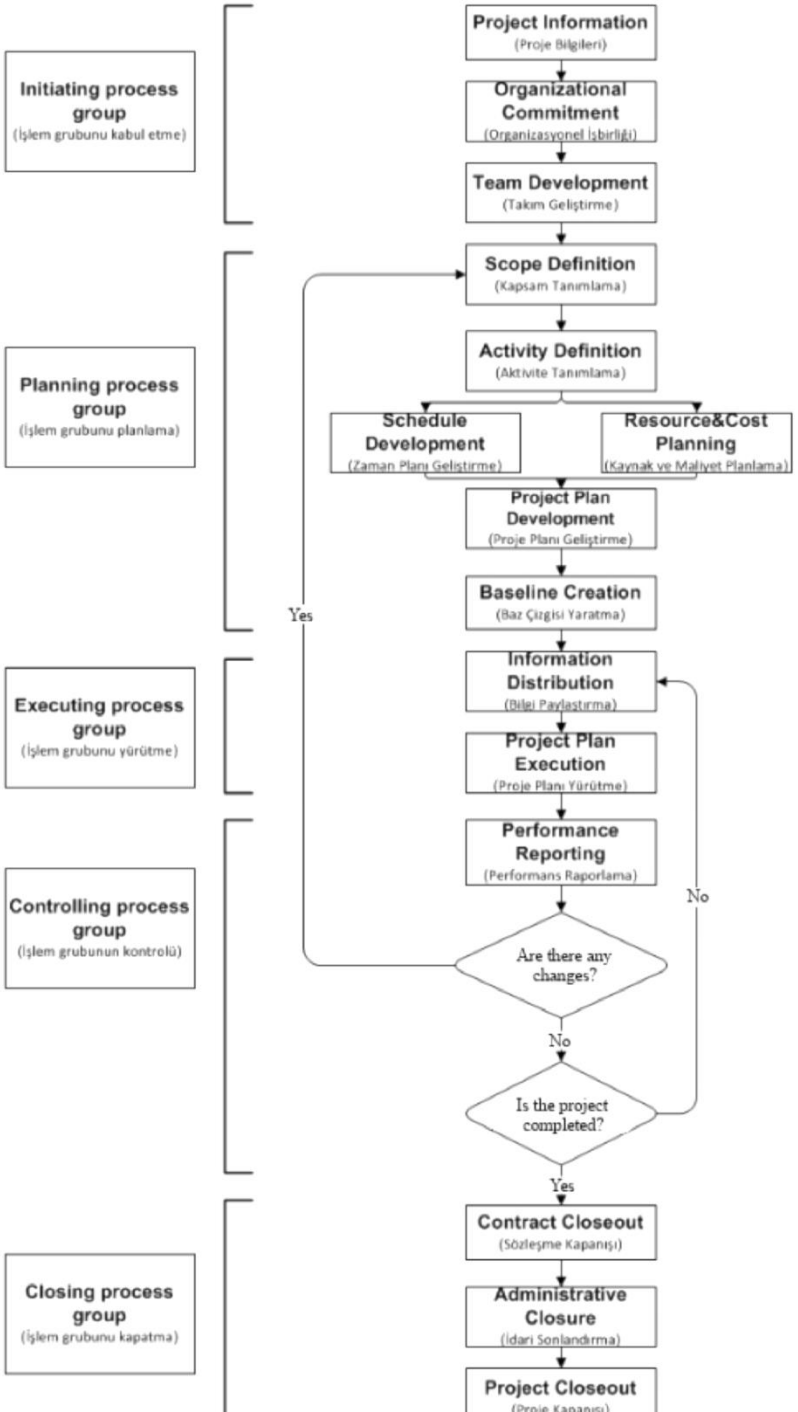
Initiating process group
(İşlem grubunu kabul etme)
Planning process group
(İşlem grubunu planlama)
Executing process group
(İşlem grubunu yürütme)
Controlling process group
(İşlem grubunun kontrolü)
Closing process group
(İşlem grubunu kapatma)
Project Information
(Proje Bilgileri)
Organizational Commitment
(Organizasyonel İşbirliği)
Team Development
(Takım Geliştirme)
Scope Definition
(Kapsam Tanımlama)
Activity Definition
(Aktivite Tanımlama)
Schedule Development
(Zaman Planı Geliştirme)
Resource&Cost Planning
(Kaynak ve Maliyet Planlama)
Project Plan Development
(Proje Planı Geliştirme)
Baseline Creation
(Baz Çizgisi Yaratma)
Information Distribution
(Bilgi Paylaştırma)
Project Plan Execution
(Proje Planı Yürütme)
Performance Reporting
(Performans Raporlama)
Are there any changes?
Yes
No
Is the project completed?
No
Yes
Contract Closeout
(Sözleşme Kapanışı)
Administrative Closure
(İdari Sonlandırma)
Project Closeout

Initiating process group

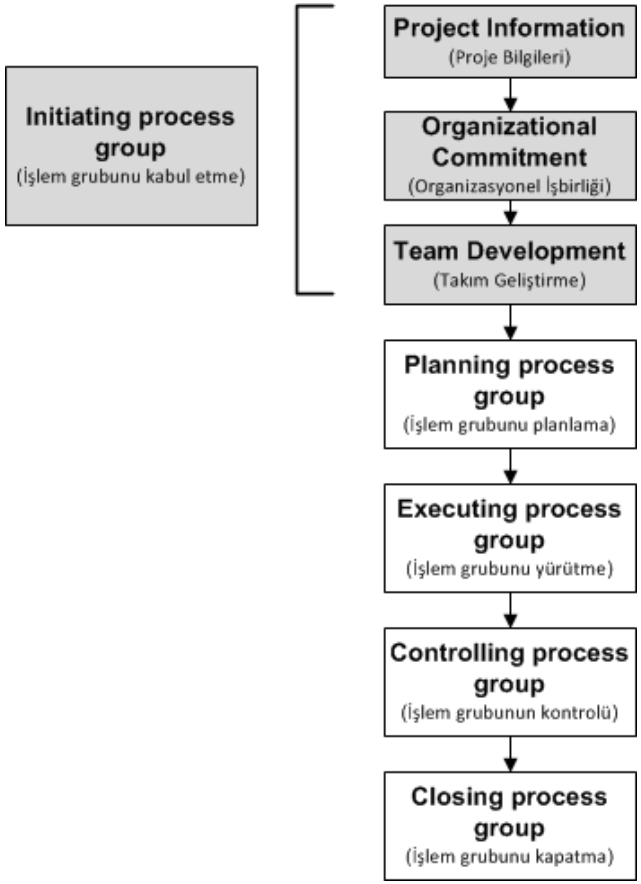

The Initiating Process Group consists of the following steps:

— Collect Project Information.
— Organizational Commitment.
— Team Development.



Initiating process group


- The initial scope is defined and initial financial resources are determined.
- Internal and external stakeholders are identified.
- The influence and objectives of the project stakeholders are revealed.
- Feasibility analysis is performed by considering the availability of the resources and applicability of the objectives of the stakeholder.

Stakeholder= all the people and organizations that are affected by the existence of the project and project's outcomes.

Purpose of Initiation Process

- To commit the organization to a project or phase
- To set the overall solution direction
- To define top-level project objectives
- To secure the necessary approvals and resources
- To validate alignment with overall business objectives
- To assign a project manager

Planning process group

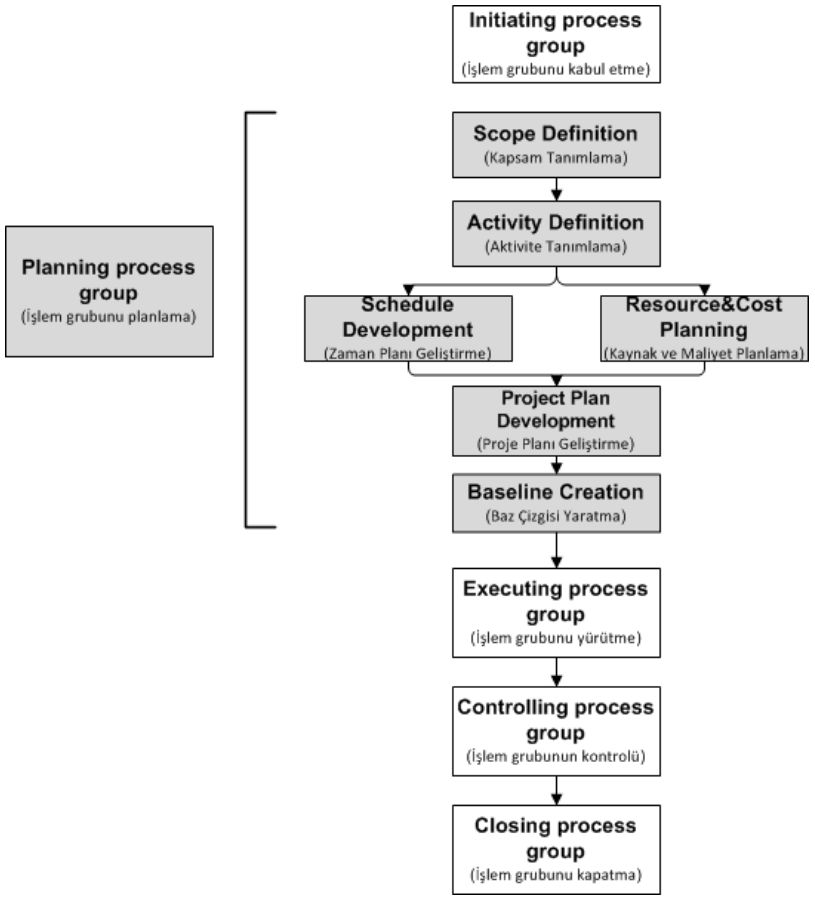


The Planning Process Group consists of the following steps:

- Scope Definition.
- Activity Definition.
- Schedule Development.
- Resource Planning.
- Cost Planning.
- Project Plan Development.
- Baseline Creation.


Planning process group

- Consists of those processes performed to establish the total scope of the effort, define and refine the objectives and develop the course of action required to achieve those objectives.
- The multi-dimensional nature of project management creates repeated feedback loops for additional analysis.
- Due to the significant changes occurring throughout the project, the planning processes are revisited to make modifications on the plans developed.
- Planning process is iterative and ongoing processes.

Review Knowledge Areas

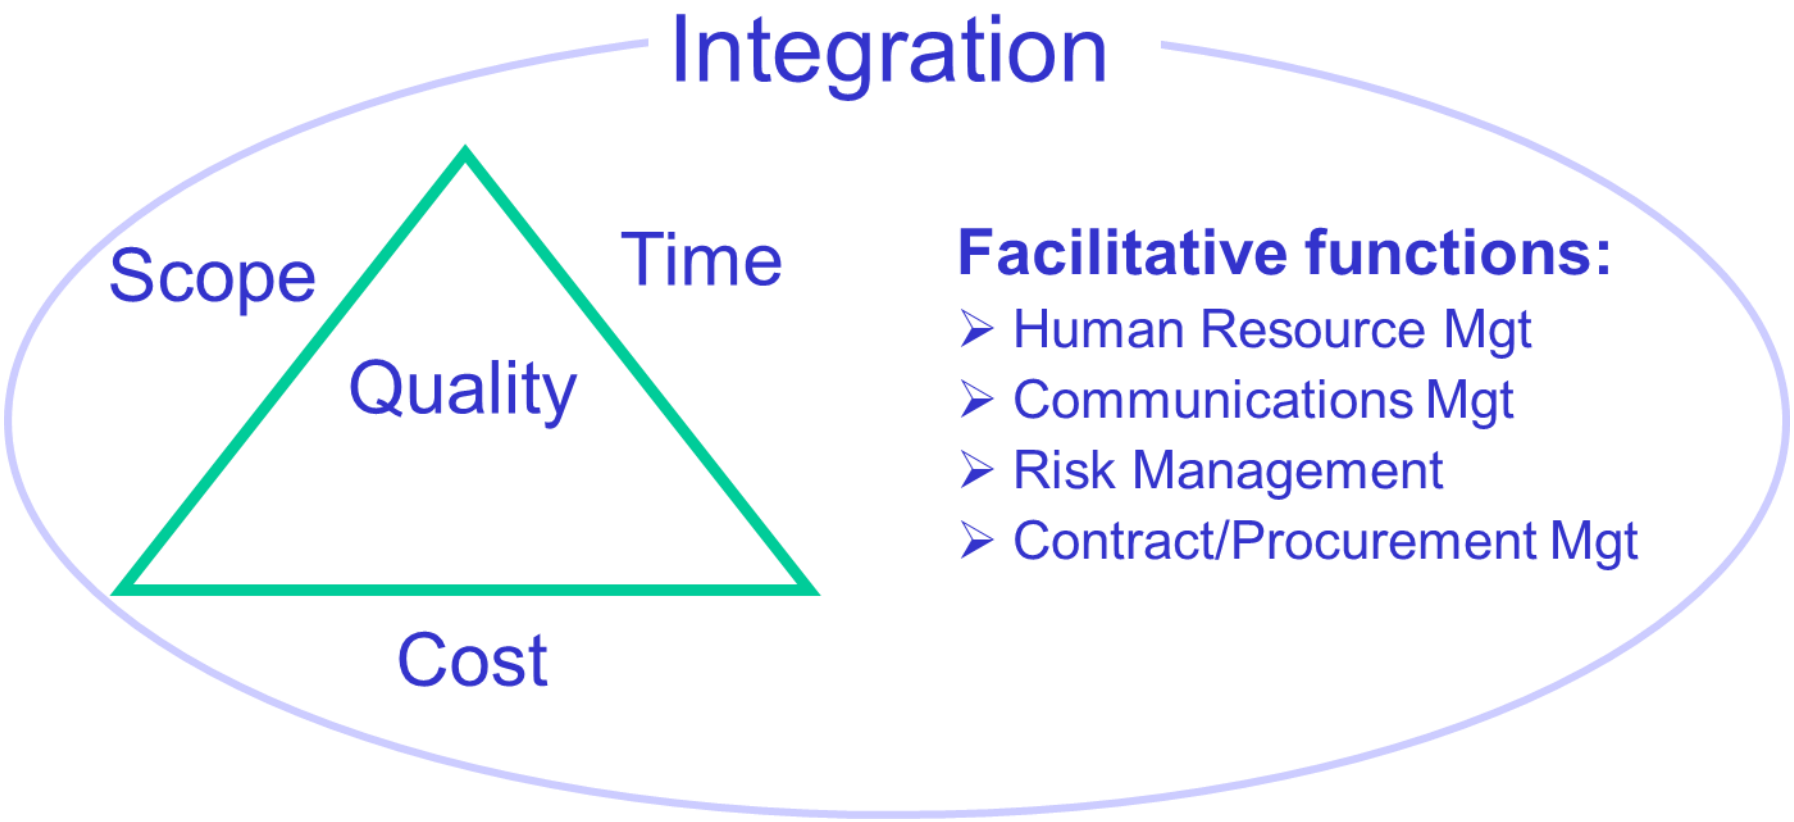

Executing Process Group

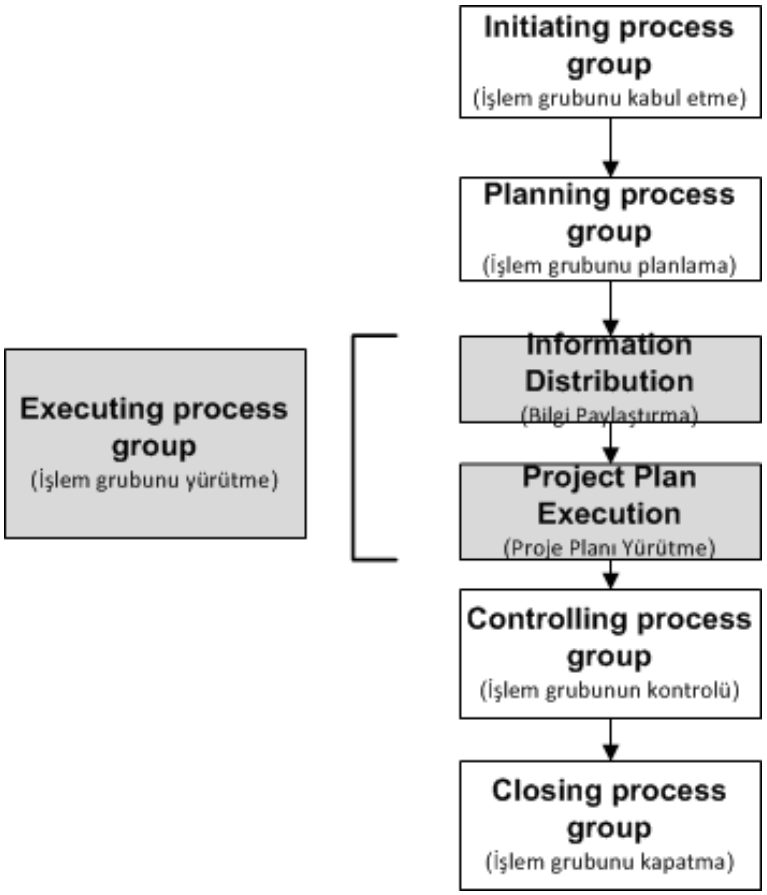


The Executing Process Group consists of the following steps:

- Information Distribution.
- Project Plan Execution.

Executing Process Group

- Consists of those processes performed to complete the work defined in the project management plan to satisfy the project specifications.
- This process group involves coordinating people and resources, as well as integrating and performing the activities of the project in accordance with project management plan.


Controlling Process Group

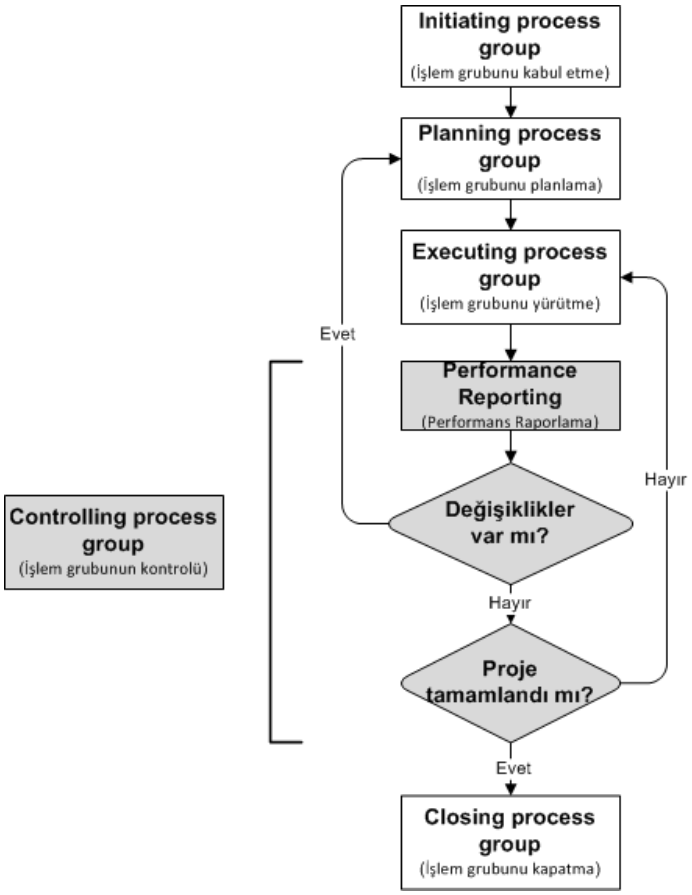

The Controlling Process Group consists of the following steps:

— Analysis and evaluation of the project.
— Recommendation of necessary actions.
— Change the project with the realistic data.
— Re-estimation of the schedule.
— Convey of the performance of the project to the project team.

Closing Process Group

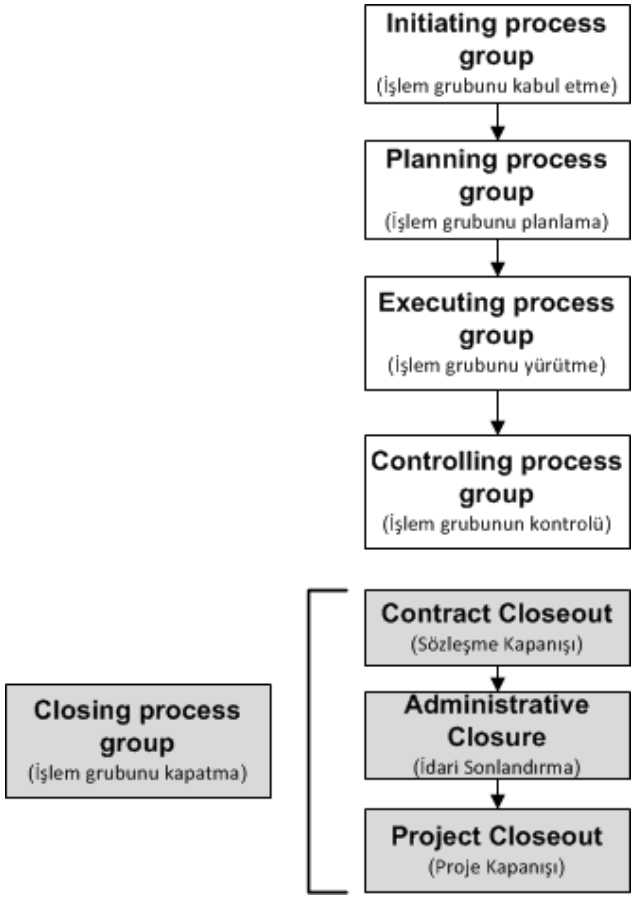

The Closing Process Group consists of the following steps:

- Contract Closeout
- Administrative closure
- Project Closeout

Contract Close Out Activities:

- Verify product/service acceptance
- Update records based on final contract results
- Archive contract documentation of completed work results
- Notification to end-user of contract completion
- Obtain formal acceptance

Administrative Close Out Activities:

- Collect all project records
- Document performance measures resulting from performance reviews, variance, trends and earned value analysis
- Formalize acceptance/signoff of the product by the sponsor, client, customer
- Archive project documentation
- Verifying project results in preparation for formal acceptance
- Create and Complete Punch List
- Conduct and Document the lessons learned
- Perform final appraisal review of team members

Project Closing – Elements:

- Administrative Close Out – Generating, gathering, disseminating information to formalize phase or project completion, including evaluating the project, compiling lessons learned for use in planning future phases or projects

- Contract Close Out – Completion and settlement of the contract including resolution of any open items

Table 1-1. Project Management Process Group and Knowledge Area Mapping

Knowledge Areas	Project Management Process Groups				
	Initiating Process Group	Planning Process Group	Executing Process Group	Monitoring and Controlling Process Group	Closing Process Group
4. Project Integration Management	4.1 Develop Project Charter	4.2 Develop Project Management Plan	4.3 Direct and Manage Project Work 4.4 Manage Project Knowledge	4.5 Monitor and Control Project Work 4.6 Perform Integrated Change Control	4.7 Close Project or Phase
5. Project Scope Management		5.1 Plan Scope Management 5.2 Collect Requirements 5.3 Define Scope 5.4 Create WBS		5.5 Validate Scope 5.6 Control Scope	
6. Project Schedule Management		6.1 Plan Schedule Management 6.2 Define Activities 6.3 Sequence Activities 6.4 Estimate Activity Durations 6.5 Develop Schedule		6.6 Control Schedule	
7. Project Cost Management		7.1 Plan Cost Management 7.2 Estimate Costs 7.3 Determine Budget		7.4 Control Costs	
8. Project Quality Management		8.1 Plan Quality Management	8.2 Manage Quality	8.3 Control Quality	
9. Project Resource Management		9.1 Plan Resource Management 9.2 Estimate Activity Resources	9.3 Acquire Resources 9.4 Develop Team 9.5 Manage Team	9.6 Control Resources	
10. Project Communications Management		10.1 Plan Communications Management	10.2 Manage Communications	10.3 Monitor Communications	
11. Project Risk Management		11.1 Plan Risk Management 11.2 Identify Risks 11.3 Perform Qualitative Risk Analysis 11.4 Perform Quantitative Risk Analysis 11.5 Plan Risk Responses	11.6 Implement Risk Responses	11.7 Monitor Risks	
12. Project Procurement Management		12.1 Plan Procurement Management	12.2 Conduct Procurements	12.3 Control Procurements	
13. Project Stakeholder Management	13.1 Identify Stakeholders	13.2 Plan Stakeholder Engagement	13.3 Manage Stakeholder Engagement	13.4 Monitor Stakeholder Engagement	
